

Request for Information

Date of Request:	July 17, 2024	RFP #:	22
		RFP Name:	Pre Bid RFIs
From:	Leah Nagy Bowman Consulting Group, Ltd. 13461 Sunrise Valley Drive, Suite 500 Herndon, VA 20171 imaslov@bowman.com	To:	Owen Weinstein architrave p.c. 420 10 th Street SE Washington, DC 20003 owen.weinstein@architravepc.com

Description:

Can we be provided with a drawing which clearly shows the location & limit of existing bituminous and concrete paving to know the extent of restoration work?

Response:

Areas labeled "brick" and "asphalt" on C112 and C113 within the LOD (limit of disturbance) should be restored to a like new condition at the conclusion of the project. "Brick" is the Olmsted Walk pavers. Match per NZP Olmsted paver detail – see attached detail and specification.

Signature:




Date:

July 25, 2024



Bowman
13455 Sunrise Blvd, Suite 100
Washington DC 20004
202.544.8442
www.bowman.com



AS SHOWN

GRAPHIC SCALE(S)


11/03/21	TITLE	DATE
11/03/21	REV	DESCRIPTION

Smithsonian Institution
600 Maryland Avenue S.W., Suite 5001
Washington DC 20004-2520


DATE	BY	DESCRIPTION
11/03/21	C 171	ISSUE FOR CONSTRUCTION

DETAIL SECTIONS

SHEET NO.	DATE	ITEM	SIZE	GRID

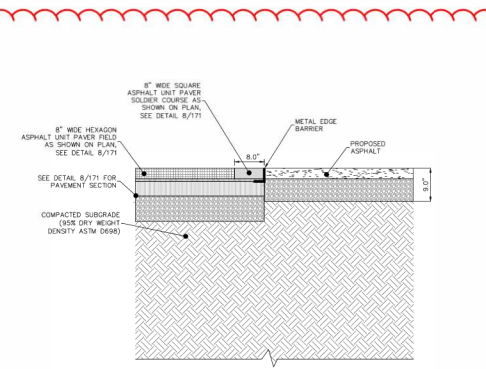

5
C 171GI
**PAVER-ASPHALT
TYPICAL SECTION** SCALE = 1" : 1'



8
C 171GI
PAVER DETAIL SCALE = NTS

PAVING SCHEDULE							
PAVER TYPE	MATERIAL	FINISH/ COLOR	SIZE	THICKNESS	JOINT TYPE/ SETTING BED	BASE	LOCATION
PV-1	HEXAGONAL ASPHALT BLOCK PAVER	GROUND TUDOR FINISH/ ABOUT	8" HEXAGON	3"	HAND TIGHT JOINT BITUMINOUS SETTING BED	BITUMINOUS	ADJACENT TO QUARTERED WALK (PAVER FIELD)
PV-2	ASPHALT BLOCK PAVER	GROUND TUDOR FINISH/ ABOUT	8" X 8" SQUARE	3"	HAND TIGHT JOINT BITUMINOUS SETTING BED	BITUMINOUS	ADJACENT TO QUARTERED WALK (PAVER FIELD BORDER)

9
C 171GI
PAVING SCHEDULE SCALE = NTS

SECTION 321400 - UNIT PAVING

PART 1 - GENERAL

1.1 RELATED DOCUMENTS

- A. Drawings and general provisions of the Contract, including General and Supplementary Conditions and Division 01 Specification Sections, apply to this Section.

1.2 SUMMARY

- A. Section Includes:
 - 1. Asphalt-block pavers set in bituminous setting beds.

1.3 PREINSTALLATION MEETINGS

- A. Preinstallation Conference: Conduct conference at Project site

1.4 ACTION SUBMITTALS

- A. Product Data: For materials other than water and aggregates.
- B. Product Data: For the following:
 - 1. Pavers.
 - 2. Bituminous setting materials.

C. LEED Submittals:

1. Product Certificates for Credit MR 5: For products and materials required to comply with requirements for regional materials, certificates indicating location of material manufacturer and point of extraction, harvest, or recovery for each raw material. Include statement indicating distance to Project, cost for each regional material, and fraction by weight that is considered regional.

D. Sieve Analyses: For aggregate setting-bed materials, according to ASTM C 136.

E. Samples for Initial Selection: For each type of unit paver indicated and the following:

1. Joint materials involving color selection.

F. Samples for Verification: For full-size units of each type of unit paver indicated and the following:

1. Joint materials
2. Asphalt Unit Pavers

1.5 INFORMATIONAL SUBMITTALS

A. Material Certificates: For unit pavers. Include statements of material properties indicating compliance with requirements, including compliance with standards. Provide for each type and size of unit.

B. Product Test Reports: Based on evaluation of comprehensive tests performed by a qualified testing agency, for unit pavers, indicating compliance with requirements.

1. For solid interlocking paving units, include test data for freezing and thawing according to ASTM C 67.

1.6 QUALITY ASSURANCE

- A. Mockups: Build mockups to verify selections made under Sample submittals, to demonstrate aesthetic effects, and to set quality standards for materials and execution.
 - 1. Subject to compliance with requirements, approved mockups may become part of the completed Work if undisturbed at time of Substantial Completion.

1.7 DELIVERY, STORAGE, AND HANDLING

- A. Store pavers on elevated platforms in a dry location. If units are not stored in an enclosed location, cover tops and sides of stacks with waterproof sheeting, securely tied.
- B. Store cementitious materials on elevated platforms, under cover, and in a dry location. Do not use cementitious materials that have become damp.
- C. Store aggregates where grading and other required characteristics can be maintained and contamination avoided.
- D. Store liquids in tightly closed containers protected from freezing.
- E. Store asphalt cement and other bituminous materials in tightly closed containers.

1.8 FIELD CONDITIONS

- A. Cold-Weather Protection: Do not use frozen materials or materials mixed or coated with ice or frost. Do not build on frozen subgrade or setting beds. Remove and replace unit paver work damaged by frost or freezing.
- B. Weather Limitations for Bituminous Setting Bed:
 - 1. Install bituminous setting bed only when ambient temperature is above 40 deg F (4 deg C) and when base is dry.

2. Apply asphalt adhesive only when ambient temperature is above 50 deg F (10 deg C) and when temperature has not been below 35 deg F (2 deg C) for 12 hours immediately before application. Do not apply when setting bed is wet or contains excess moisture.

PART 2 - PRODUCTS

2.1 MANUFACTURERS

- A. Source Limitations: Obtain each type of unit paver, joint material, and setting material from single source with resources to provide materials and products of consistent quality in appearance and physical properties.

2.2 ASPHALT-BLOCK PAVERS

- A. Asphalt-Block Pavers: Solid units made from asphalt cement complying with ASTM D 312, Type III; inorganic stone dust or cement filler; and coarse aggregate, consisting of clean, hard, unweathered stone crushed into angular particles varying in size up to 3/8 inch (9.5 mm).

1. Paver PV-1 (as shown on plan): Basis of design manufacturer: Hanover Architectural Products. www.hanoverpavers.com.
 - a. Face Size: 8" Hexagonal
 - b. Finish: Ground Tudor Finish
 - c. Color: Matrix A80011
 - d. Location: Olmsted Walk Main Field Paver
2. Paver PV-2 (as shown on plan): Basis of design manufacturer: Hanover Architectural Products. www.hanoverpavers.com.
 - a. Face Size: 8"x8" square
 - b. Finish: Ground Tudor Finish

- c. Color: Matrix A80026
- d. Location: Border edge paver for Olmsted Walk

2.3 BITUMINOUS SETTING-BED MATERIALS

- A. Primer for Base: ASTM D 2028/D 2028M, cutback asphalt, grade as recommended by unit paver manufacturer.
- B. Fine Aggregate for Setting Bed: ASTM D 1073, No. 2 or No. 3.
- C. Asphalt Cement: ASTM D 3381/D 3381M, Viscosity Grade AC-10 or Grade AC-20.
- D. Neoprene-Modified Asphalt Adhesive: Paving manufacturer's standard adhesive consisting of oxidized asphalt combined with 2 percent neoprene and 10 percent long-fibered mineral fibers containing no asbestos.
- E. Sand for Joints: Fine, sharp, washed, natural sand or crushed stone with 100 percent passing No. 16 (1.18-mm) sieve and no more than 10 percent passing No. 200 (0.075-mm) sieve.
 - 1. Provide sand of color needed to produce required joint color.

2.4 BITUMINOUS SETTING-BED MIX

- A. Mix bituminous setting-bed materials at an asphalt plant in approximate proportion, by weight, of 7 percent asphalt cement to 93 percent fine aggregate unless otherwise indicated. Heat mixture to 300 deg F (149 deg C).

PART 3 - EXECUTION

3.1 EXAMINATION

- A. Examine surfaces indicated to receive unit paving, with Installer present, for compliance with requirements for installation tolerances and other conditions affecting

performance.

- B. Where unit paving is to be installed over waterproofing, examine waterproofing installation, with waterproofing Installer present, for protection from paving operations, including areas where waterproofing system is turned up or flashed against vertical surfaces.
- C. Proceed with installation only after unsatisfactory conditions have been corrected and waterproofing protection is in place.

3.2 PREPARATION

- A. Remove substances from concrete substrates that could impair mortar bond, including curing and sealing compounds, form oil, and laitance.
- B. Sweep concrete substrates to remove dirt, dust, debris, and loose particles.
- C. Proof-roll prepared subgrade according to requirements in Section 312000 "Earth Moving" to identify soft pockets and areas of excess yielding. Proceed with unit paver installation only after deficient subgrades have been corrected and are ready to receive base course for unit pavers.

3.3 INSTALLATION, GENERAL

- A. Do not use unit pavers with chips, cracks, voids, discolorations, or other defects that might be visible or cause staining in finished work.
- B. Mix pavers from several pallets or cubes, as they are placed, to produce uniform blend of colors and textures.
- C. Cut unit pavers with motor-driven masonry saw equipment to provide clean, sharp, unchipped edges. Cut units to provide pattern indicated and to fit adjoining work neatly. Use full units without cutting where possible. Hammer cutting is not acceptable.

- D. Joint Pattern: As indicated
- E. Tolerances: Do not exceed 1/32-inch (0.8-mm) unit-to-unit offset from flush (lippage) nor 1/8 inch in 10 feet (3 mm in 3 m) from level, or indicated slope, for finished surface of paving.
- F. Provide steel edge barrier between pavers and asphalt as indicated on paving plans and details. Install edge restraints before placing unit pavers.

3.4 BITUMINOUS SETTING-BED APPLICATIONS

- A. Apply primer to concrete slab or binder course immediately before placing setting bed.
- B. Prepare for setting-bed placement by locating 3/4-inch- (19-mm-) deep control bars approximately 11 feet (3.3 m) apart and parallel to one another, to serve as guides for striking board. Adjust bars to subgrades required for accurate setting of paving units to finished grades indicated.
- C. Place bituminous setting bed where indicated, in panels, by spreading bituminous material between control bars. Spread mix at a minimum temperature of 250 deg F (121 deg C). Strike setting bed smooth, firm, even, and not less than 3/4 inch (19 mm) thick. Add fresh bituminous material to low, porous spots after each pass of striking board. After each panel is completed, advance first control bar to next position in readiness for striking adjacent panels. Carefully fill depressions that remain after removing depth-control bars.
 - 1. Roll setting bed with power roller to a nominal depth of 3/4 inch (19 mm). Adjust thickness as necessary to allow accurate setting of unit pavers to finished grades indicated. Complete rolling before mix temperature cools to 185 deg F (85 deg C).
- D. Apply neoprene-modified asphalt adhesive to cold setting bed by squeegeeing or troweling to a uniform thickness of 1/16 inch (1.6 mm). Proceed with setting of paving units only after adhesive is tacky and surface is dry to touch.
- E. Place pavers carefully by hand in straight courses, maintaining accurate alignment and

uniform top surface. Protect newly laid pavers with plywood panels on which workers can stand. Advance protective panels as work progresses, but maintain protection in areas subject to continued movement of materials and equipment to avoid creating depressions or disrupting alignment of pavers. If additional leveling of paving is required, and before treating joints, roll paving with power roller after sufficient heat has built up in the surface from several days of hot weather.

- F. Joint Treatment: Place unit pavers with hand-tight joints. Fill joints by sweeping sand over paved surface until joints are filled. Remove excess sand after joints are filled.

3.5 REPAIRING, POINTING, AND CLEANING

- A. Remove and replace unit pavers that are loose, chipped, broken, stained, or otherwise damaged or that do not match adjoining units. Provide new units to match adjoining units and install in same manner as original units, with same joint treatment and with no evidence of replacement.
- B. Pointing: During tooling of joints, enlarge voids or holes and completely fill with grout. Point joints at sealant joints to provide a neat, uniform appearance, properly prepared for sealant application.
- C. Cleaning: Remove excess grout from exposed paver surfaces; wash and scrub clean.
 - 1. Remove temporary protective coating as recommended by coating manufacturer and as acceptable to paver and grout manufacturers.
 - 2. Do not allow protective coating to enter floor drains. Trap, collect, and remove coating material.

END OF SECTION
